

2 Dyke Road Proposed third floor apartment

Cubed Property Advisors Limited

16 Nov 2023

<http://www.cubedltd.co.uk>


Project manager	
Project dates	5 Feb 2024 - 29 Mar 2025
Completion	0%
Tasks	32
Resources	0

Proposed third floor apartment
Maintenance Repair and Wind and Watertight works.
2 Dyke Road
Brighton
BN1 3FE

Tasks

Name	Begin date	End date
Start	05/02/2024	05/02/2024
Site set up	06/02/2024	12/02/2024
Scaffold front	13/02/2024	19/02/2024
Scaffold side	20/02/2024	26/02/2024
Scaffold rear and roof	27/02/2024	07/03/2024
Sheeting	08/03/2024	14/03/2024
Structural inspection	15/03/2024	21/03/2024
Structural designs	22/03/2024	11/04/2024
Lintel repairs - Phased	12/04/2024	23/05/2024
Repointing	24/05/2024	04/07/2024
Window measures	24/05/2024	06/06/2024
Window orders	07/06/2024	18/07/2024
Structural measures steelwork	19/07/2024	01/08/2024
Roof canopy scaffold	02/08/2024	15/08/2024
Steel sign off design	02/08/2024	29/08/2024
Steelwork lead in	30/08/2024	10/10/2024
Existing Window install	16/08/2024	26/09/2024
Fascade Steel base nodes	30/08/2024	12/09/2024
Steel frame	11/10/2024	07/11/2024
Brickwork facades	08/11/2024	19/12/2024
Roof deck and timber	20/12/2024	16/01/2025
Strip original roof remove plant room	17/01/2025	24/01/2025
Relocate services	07/02/2025	27/02/2025
First fix service infras	28/02/2025	13/03/2025
Roof deck and weathering	17/01/2025	06/02/2025
New windows	07/02/2025	20/02/2025
Clean down strucure	21/02/2025	27/02/2025
Bird protection	21/02/2025	27/02/2025
Snagging	21/02/2025	13/03/2025
Internal fit out commence others	21/02/2025	20/03/2025
Strike scaffold	14/03/2025	27/03/2025
External works complete	28/03/2025	28/03/2025

Gantt Chart

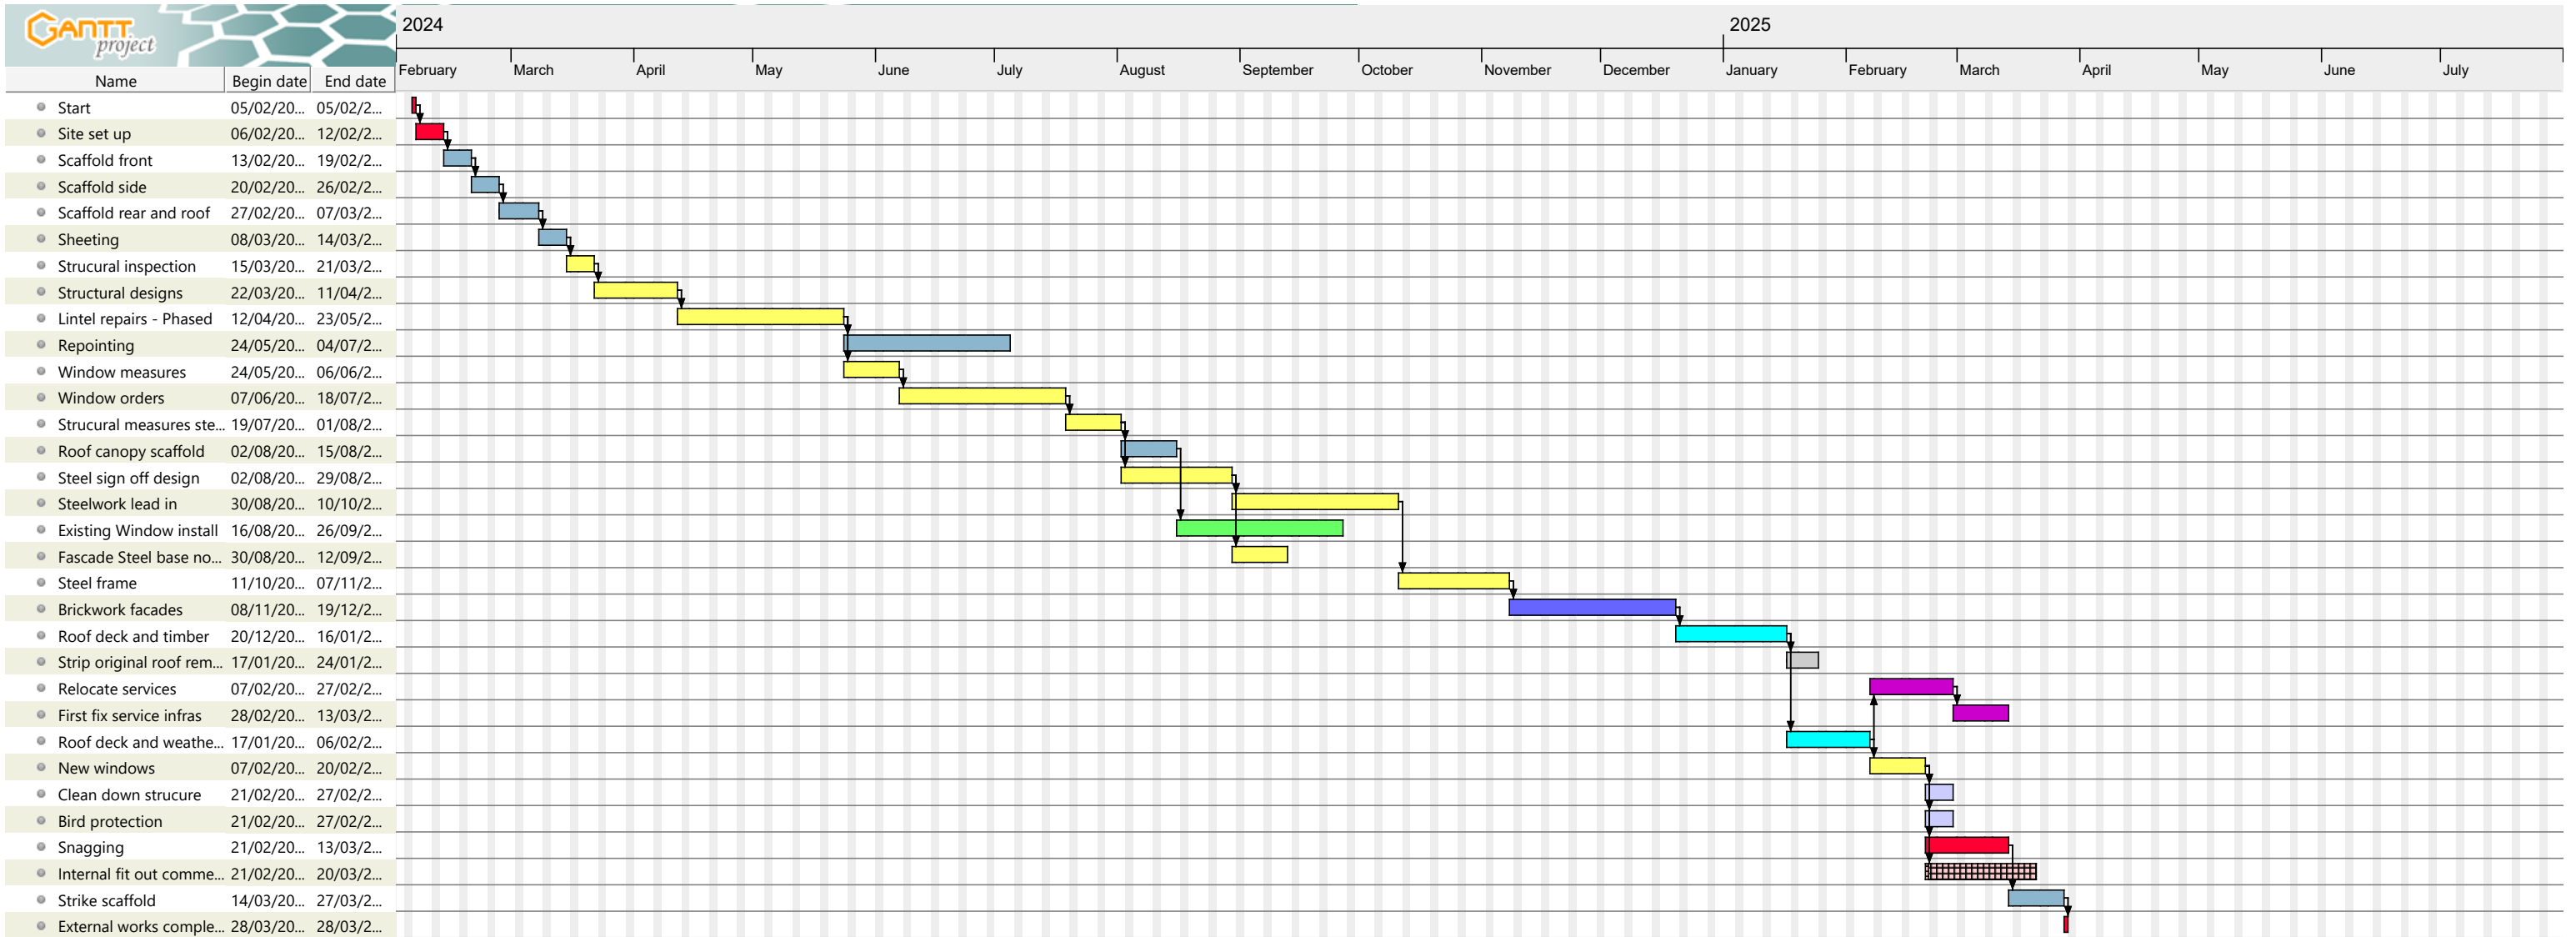

Resources Chart

