



All Saints Roman Catholic School

Site set up
Form haul roads
Divert existing services
Install attenuation
Piling mat

- Site setup
- Tree crowning to access road 
- Tree removal to rear of existing school 
- Services diversions
- Drainage diversions
- Piling Mat

New temp access to sports pitch

School parking maintained

Vehicle delivery route

Contractor Access

Area already investigated

Site turnstile

Vehicle Turning

Contractor Traffic Routes


School Circulation Routes

October 2023- November 2023 weeks 1-9



All Saints Roman Catholic School

- Section 80
- Bat Surveys
- Demolition Phase A
- Asbestos strip Phase B
-

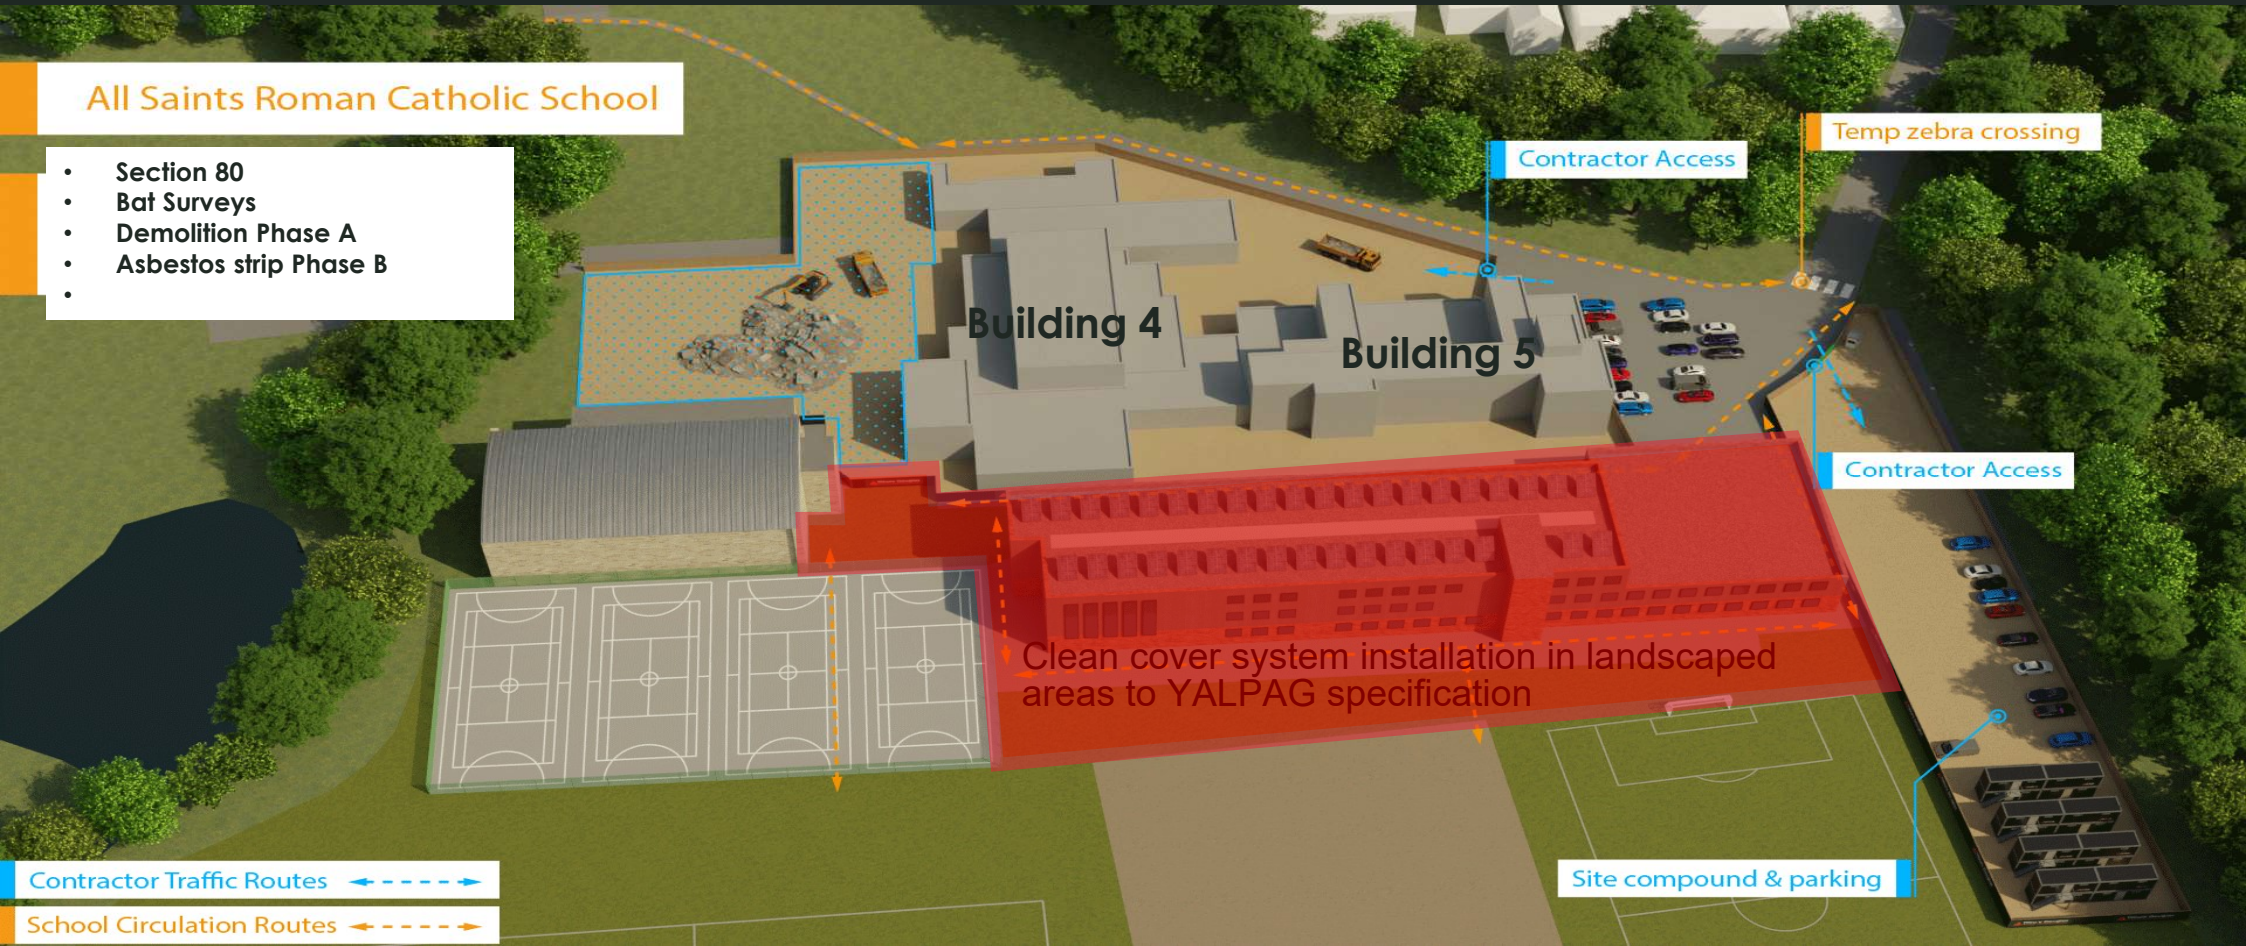

March – April 2025 week 73- 77



All Saints Roman Catholic School

- Phase B Demo
- Reduce dig areas

Sampling for waste assessment purposes

New footpath route

New school temp parking

Contractor access

Temp zebra crossing

Building 4

Building 5

Contractor Access

Contractor Traffic Routes

School Circulation Routes

Investigations to comprise trial pitting of shallow soils and sampling (soil suite, asbestos screen, WAC) in one with the identified Contaminants of Concern

April - 2025- July 2025 week 83-93

All Saints Roman Catholic School

Demolition of existing school
Area 1 Externals
Formation of new parking,
tennis courts & external
areas

Sampling for waste soils assessment and contaminated land risk assessments - to include discovery strategy for any boiler rooms, fuel storage tanks or buried asbestos beneath the floor slab

New footpath route

Contractor access

Temp zebra crossing

Contractor Access

School parking

Investigations to comprise Trial Pitting and sample analysis of shallow soils for Soil Suite, asbestos screen and any other CoCs following discovery strategy

Contractor Traffic Routes

School Circulation Routes

Site compound & parking



All Saints Roman Catholic School

- Form tennis courts
- RT walls
- PV canopies
- Drainage
- Services
- Hard & soft Landscaping

Installation of clean cover system and other remediation based upon the results of the additional investigation

Contractor access

Temp zebra crossing

Contractor Access

Area handed over

Site compound & parking

Contractor Traffic Routes

School Circulation Routes

July 2025 – October 2025 week 82- 99

All Saints Roman Catholic School

Project Completion



October 25 week 100

