

Proposed stone access track (ground level)

Proposec
Proposec

Diverl
Line of E

Tucke

Tree Protection Specification

All vegetation identified for removal should be removed prior to the start of works. The Tree Protection Plan provides details of vegetation removals and relocations.

An assessment of crown impacts should be carried out by the Consultant Arboriculturist or the Client's Landscape Manager prior to implementing tree protection, so that any potential requirements for access pruning have been assessed.

Any access pruning should be carried out prior to the installation of the Tree Protection Fencing and carried out to the standards set out in BS5837:2012 Tree Works - Recommendations.

The Protection Fencing should be to the specification below:

Figure 1 - Examples of above-ground stabling systems

Tree Protection should be formed from Herafex fencing panels secured with anti-tamper clips and with supports fixed into the ground to prevent movement once installed. Manufacturers' recommendations should be provided to ensure correct installation.

All personnel should be made aware of the protected areas and instructed to keep them free of materials, waste and excess soil. Soil disturbance should be prohibited and control of any kind, including foot traffic, should also be excluded within the root protection area (RPA) unless previously agreed and adequate ground protection has been installed. Where foot traffic is agreed within the RPA, single thickness scaffold boards laid over a compressible material or a geotextile, or supported by scaffold should suffice. Where vehicle access through the RPA is agreed an engineer should be consulted to design adequate ground protection methods.

© 2020 RPS Group
Notes:
1. This drawing has been prepared in accordance with the scope of RPS's appointment with its client and is subject to the terms and conditions of that appointment. RPS accepts no liability for any use of this document other than by its client and only for the purposes for which it was prepared and provided.
2. If received electronically it is the recipient's responsibility to print in correct scale. Only written dimensions should be used.
3. Where applicable Ordnance Survey (© Crown Copyright 2020) All rights reserved. Licence number 0100031873

Key

- Individual tree to be retained
- Individual tree requiring removal to facilitate the development
- Tree group to be retained
- Tree group to be removed
- Scrub/Hedge/Shrubs/Saplings to be retained
- Scrub/Hedge/Shrubs/Saplings to be removed

BS 5837:2012 Tree Quality Categories - Table 1

- Category A - High quality
- Category B - Moderate quality
- Category C - Low quality
- Category U - Unsuitable for retention

Root protection area (RPA) calculated in accordance with Section 4.6 - BS5837:2012


Construction Exclusion Zone - Protective fencing (e.g. Herafex style) To be assembled in accordance with Section 6.2 - BS5837:2012 (see inset for example barriers)

Security Fencing: This will provide tree protection for majority of site but must be installed prior to construction works.

Hard surfaces to be constructed above existing ground level using 'No-Dig' construction methods (see Arboricultural Practice Note 12)

NOTES:

- Refer to RPS Tree Schedule for further details.
- Survey based on a visual inspection from the ground and is not intended as a full arboricultural inspection.
- Plan produced in accordance with recommendations set out in BS 5837:2012 - 'Trees in Relation to design, demolition and construction'.
- Due to the legal protection afforded to breeding birds vegetation removal should not take place during the bird nesting period, generally, although not restricted to, March - August inclusive.
- Survey plotted using sub metre GPS survey device onto Topographical Survey provided by the client.

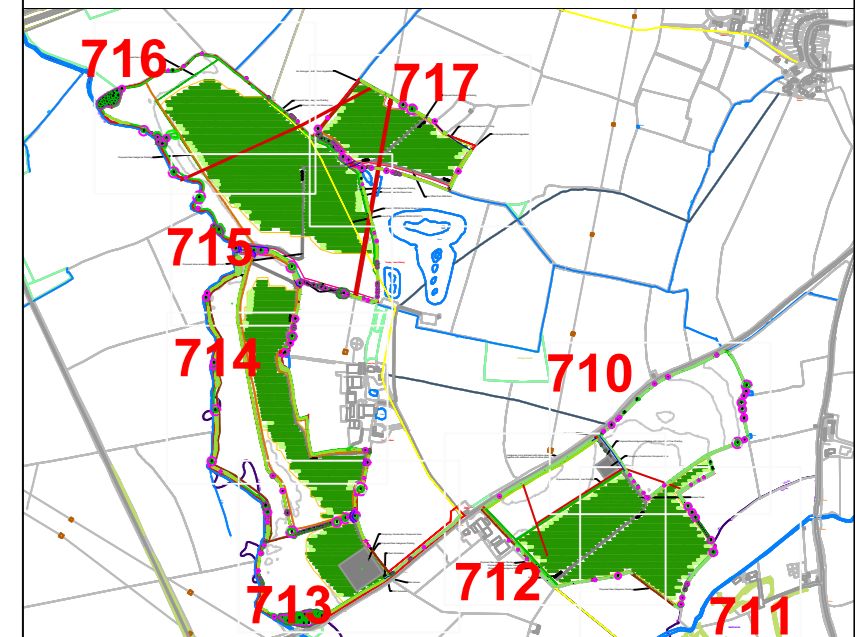

Rev	Description	By	CB	Date
B	Transferred to new template	TF	BW	Aug 23
A	First issue	TF	BW	Feb 19

rps
A TETRA TECH COMPANY

Lakesbury House, Hittingbury Road, Chandlers Ford, Hampshire SO53 5SS
T: 02380 810 440 E: rps@rpsgroup.com

Client: **SCOTTISHPOWER**

Project: **Land at Tuckey Farm, Winslow**

Title: **Tree Protection Plan**

Status: For planning
Drawn By: TF
PM/Checked by: BW

Job Ref: JSL3012
Scale @ AD: 1:500
Date Created: Aug 23

RPS Drawing / Figure Number: 715
Rev: B

rpsgroup.com

