

Site Westcroft Somerton Rd Hartest
 Date of survey 11/08/2022
 Surveyor J Choat

Plan Number	Tree Number	Species	Age	Height in m	Condition	Recommendations	Informed by risk	
							Work Priority	Inspection
1	T1	Common Lime <i>Tilia x europaea</i>	M	19	Stem forks at 0.3m to form 2 co-dominant stems, compression fork formed with included basal union. Stem welding at 1m. Occasional deadwood within crown approx. 10cm dia mostly on the south / western aspect. Leaves appear to be good size, shape and colour for time of year. Tree causing shading in summer months limiting use of patio and conservatory during morning / midday.	Reduce crown height by 3m. Reduce lateral spread by 2m. Raise crown to 6-7m removing 6 lowest primary laterals around the circumference of the stem (approx. 10-25cm dia). Remove remaining sub-laterals to achieve crown clearance of 6-7m.	3	3
1	T2	Lawsons cypress (Blue) <i>Chamaecyparis lawsoniana</i>	M	12	Twin stem. Slightly sparse higher crown. Tree causing shading in summer months limiting use of patio and conservatory during morning / midday.	Fell and grind stump following below ground service check.	3	0
1	T3	Lawsons cypress (Gold) <i>Chamaecyparis lawsoniana</i>	M	11	Crown spread and height limiting lateral growth of adjacent copper beech.	Fell in favour of adjacent copper beech.	3	0
1	T4	Purple plum <i>Prunus cerasifera nigra</i>	M	7	<i>Phellinus sp</i> at 1m on stem. Low included basal union. Decay pockets at various locations on stem and crown structure. Branch recently failed at 2m and resting on BT service.	Fell and grind stump following below ground service check.	3	0

Key

Age

Y = Young 1st 3rd of life
 EM = Early mature 2nd 3rd of life
 M = 3rd 3rd of life
 OM = Over mature, over normal life expectancy

Work Priority

1 High Works required immediately to make tree safe
 2 Moderate Works required within 4 month
 3 Low Works required within 12 -24 months as part of routine management
 0 No works required

Inspection Frequency

1 Urgent Carryout detailed inspection of the aerial parts and/or with the use of decay inspection equipment
 2 High 12 months inspection
 3 Low Low 3 year inspection
 0 None No target exists or is excluded

Tree

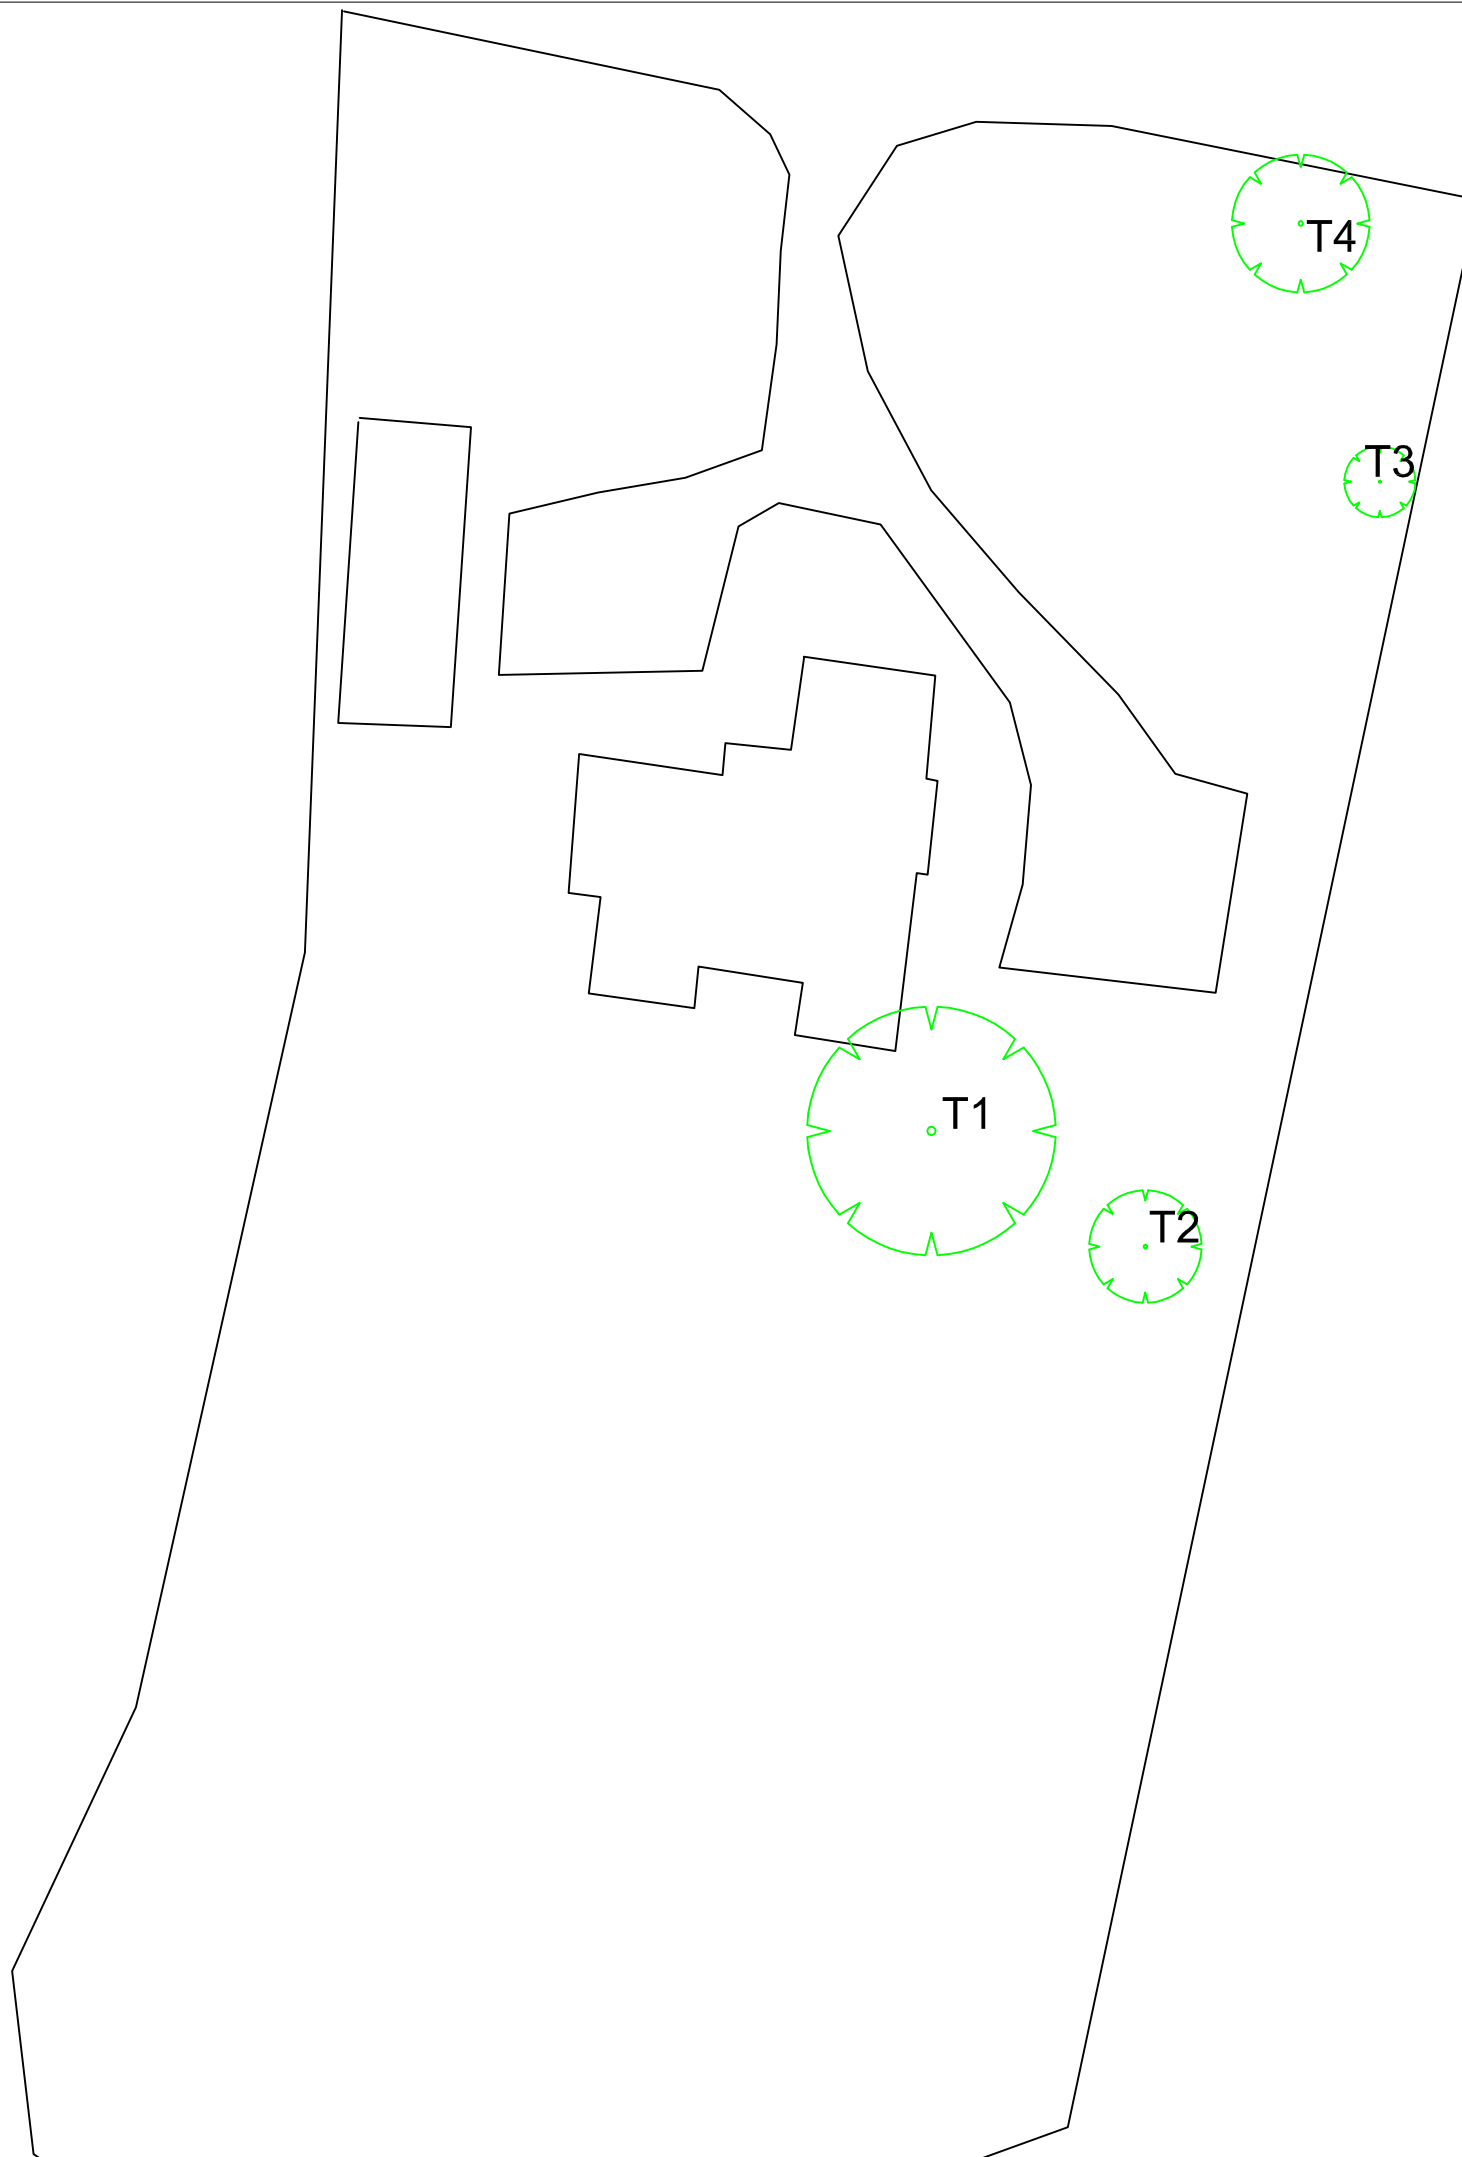


Photo 1 T1



Photo 2 T2



Photo 3 T3 (T3 right of copper beech)



Photo 4 T4 Branch torn and resting on BT service

