

The hazards noted are in addition to the normal hazards and risks faced by a competent contractor when dealing with the type of works detailed on this drawing.

CONSTRUCTION RISKS:


1. Confined spaces entry and hazardous waste materials / gas.
2. Deep manholes / excavations
3. Contractor to locate services prior to excavating.
4. Asbestos may be present.
5. Drainage connection requires deep excavation temp works required.
6. Existing drains to be protected and bridged over where required.
7. Works adjacent to busy road and river. Watercourse / ditch levels may rise rapidly following prolonged periods of rainfall.
8. Soft ground during construction works particularly in wet weather.

MAINTENANCE/CLEANING RISKS:

1. Pavement deformations to be monitored to ensure that designed pavement falls are maintained. If significant deformation is allowed to propagate then localised flooding could occur.
2. Silt traps, drainage channels, permeable pavements and inspection chambers require the standard periodic inspection regime and cleaning routine to ensure continued performance and reduce the risk of flooding.
3. Works adjacent to Watercourse / ditch. Watercourse / ditch levels will vary during heavy rainfall events.
4. Potential for soft spots within existing ground after heavy rainfall.
5. Existing live services and utilities.
6. Deep manholes / excavations - appropriate entry equipment required.
7. Soft ground during construction works particularly in wet weather.

DEMOLITION / ADAPTION RISKS:

1. Apparatus located in landscaped areas has not been designed to support heavy vehicle loading.
2. The surface water drainage apparatus has been designed to accommodate the designed catchment area, no additional areas of hardstanding can be connection into the system without risk of localised flooding on site.
3. Hazardous waste materials / dust and debris released into the air.
4. Deep manholes / excavations - appropriate entry equipment required.
5. Works adjacent to river. Watercourse / ditch levels will vary during heavy rainfall events.
6. Unknown ground conditions during / after heavy rainfall.
7. Soft ground during construction works particularly in wet weather.



PRELIMINARY DRAWING:

This drawing is for preliminary purposes only and must not be read as a construction issue. The design is not fixed and design changes are likely.

Rev	Date	Description	By	Check
P1	28/07/23	Preliminary	RB	PP

Copyright: The copyright of this drawing is vested in Schema Engineering Ltd. To be read in conjunction with all other project related drawings, reports and surveys etc. It shall not be used without permission by anyone for any purpose. Do not scale this drawing electronically or manually. Work to figured dimensions only. All dimensions are in metres unless stated otherwise. Do not turn on layers that have been turned off. Do not thaw layers that have been frozen.

Client
Cockledge Building Contractors

Project
Barrett's Lane, Needham Market
Suffolk
IP68DL


Title
Engineering Layout
Sheet 5

Scale @ A1 1:100 Status Preliminary



Date	Job Number	By	Checked By
July 2023	0304	RB	JRS

Drawing No.	Revision
C410	P1

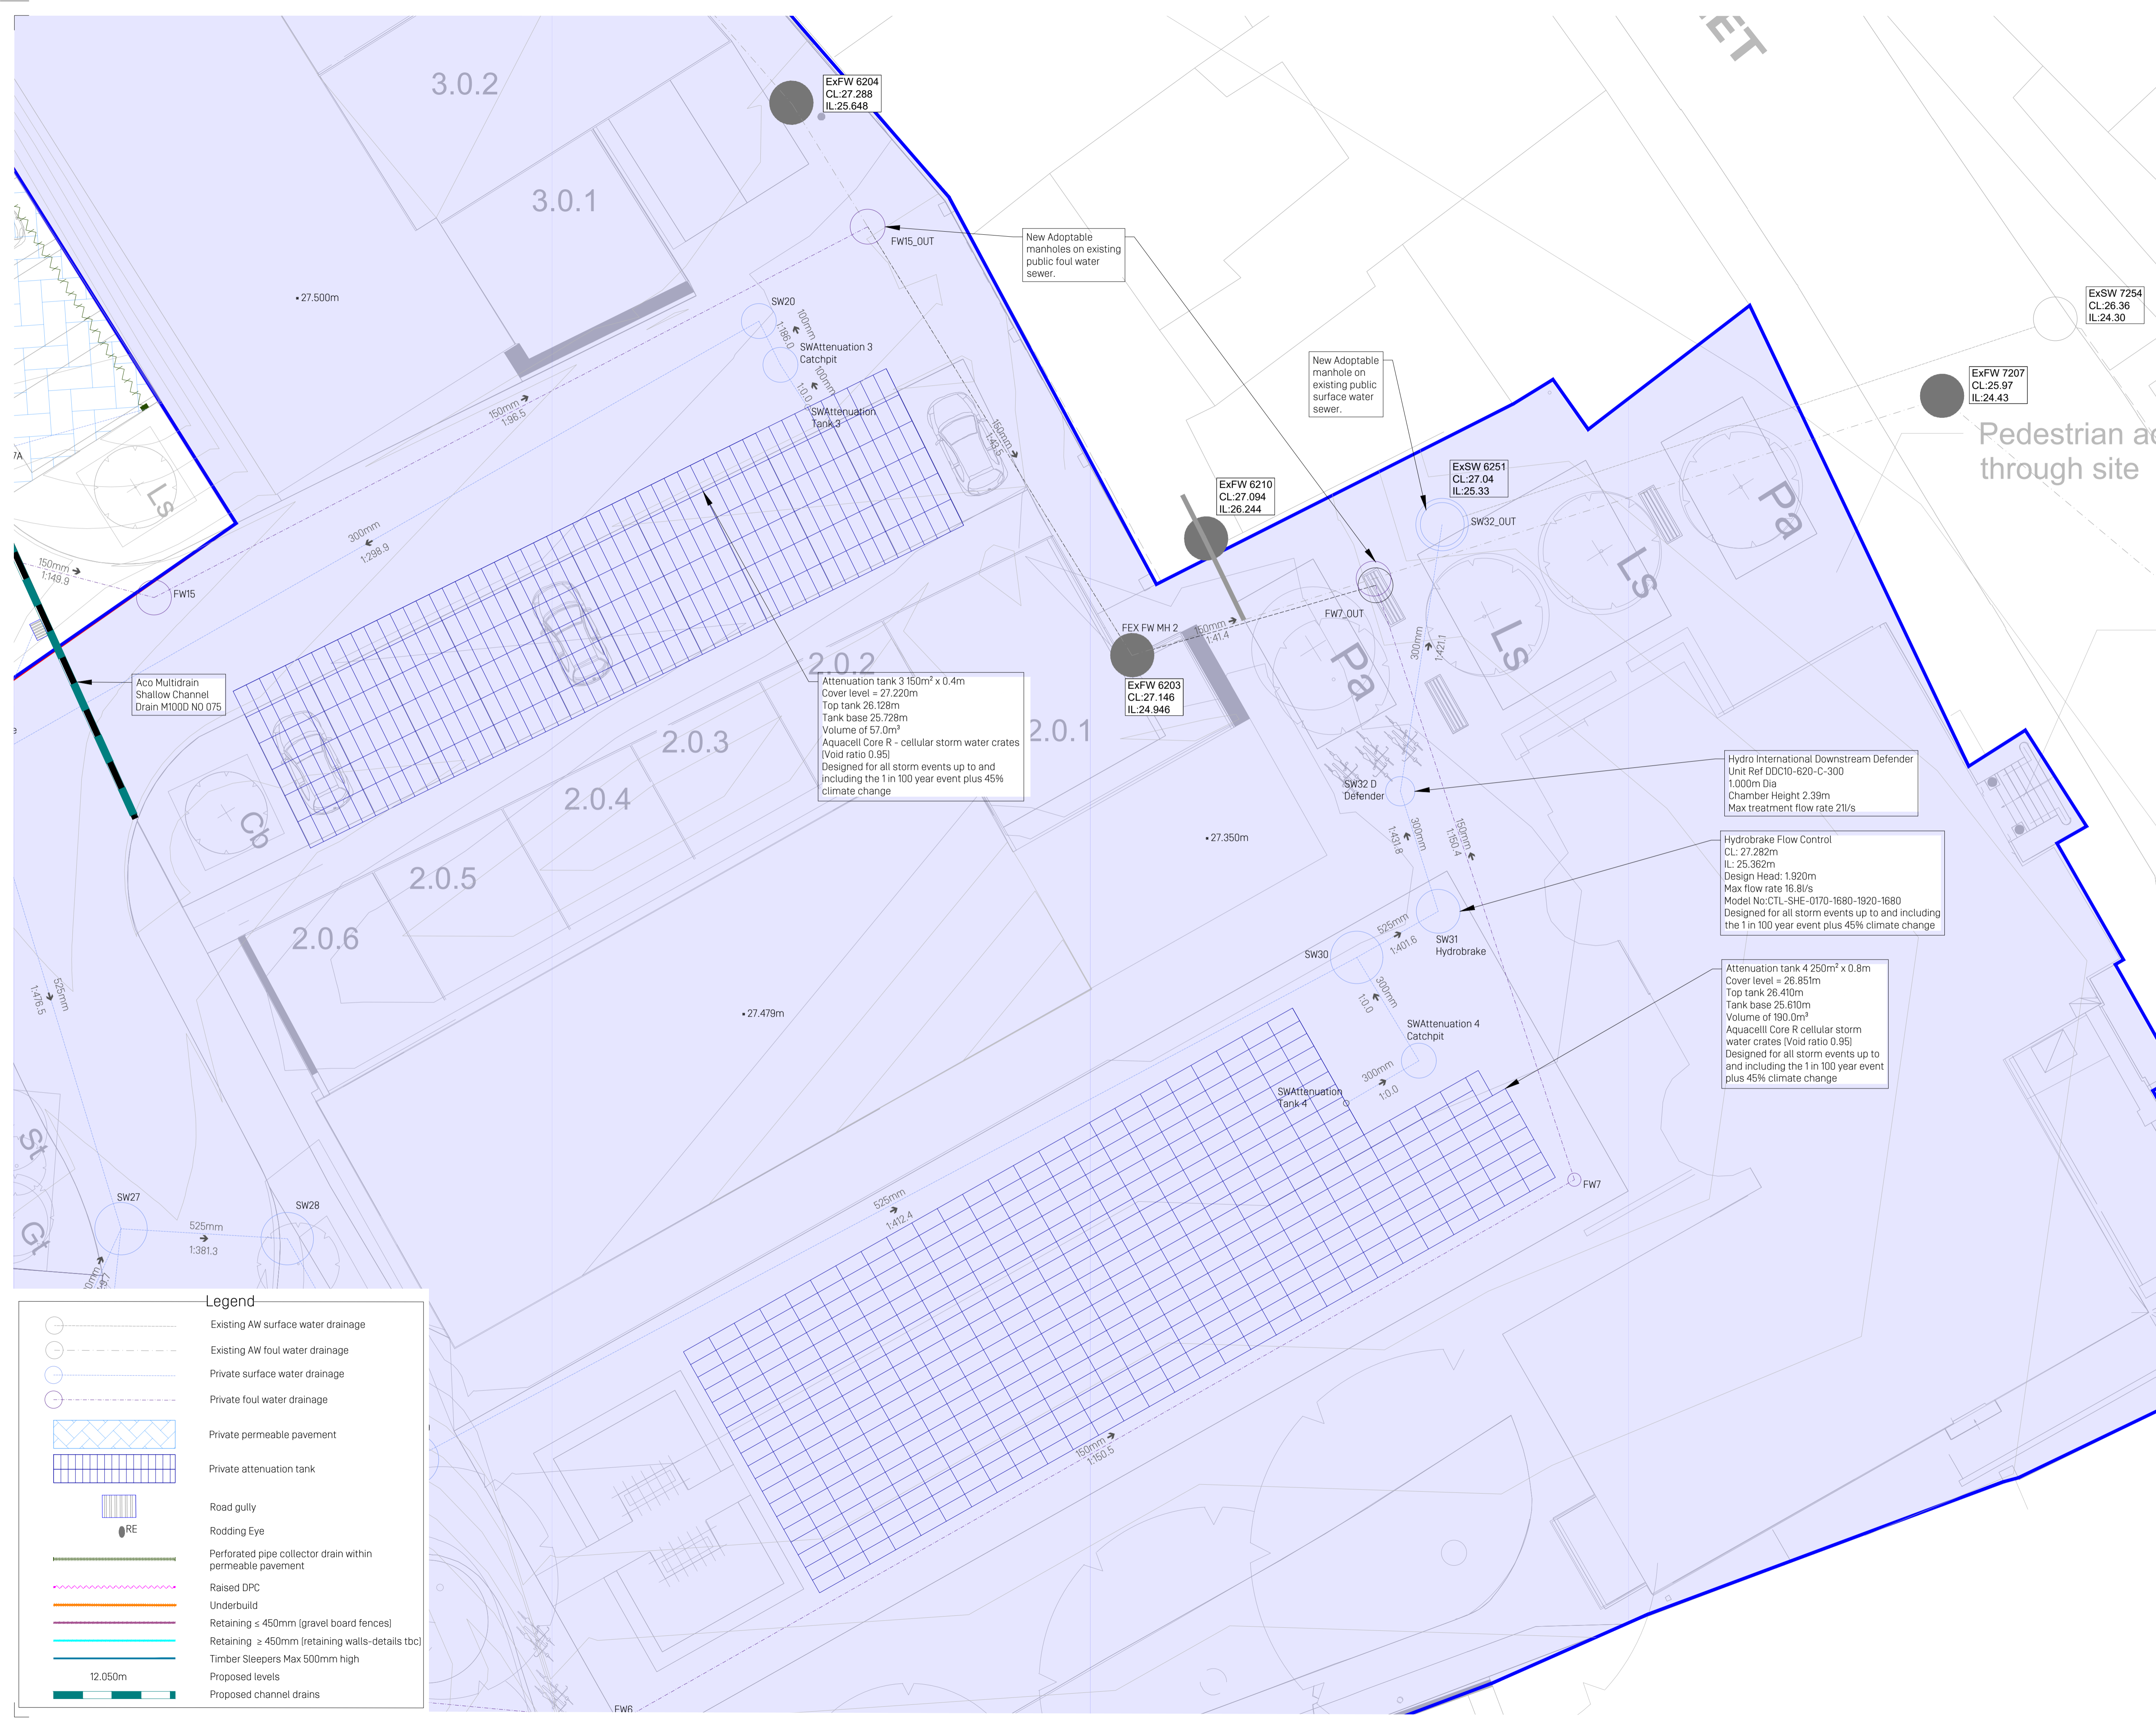

Legend

- Existing AW surface water drainage
- Existing AW foul water drainage
- Private surface water drainage
- Private foul water drainage
- Private permeable pavement
- Private attenuation tank
- Road gully
- Rodding Eye
- Perforated pipe collector drain within permeable pavement
- Raised DPC
- Underbuild
- Retaining ≤ 450mm (gravel board fences)
- Retaining ≥ 450mm (retaining walls-details tbc)
- Timber Sleepers Max 500mm high
- Proposed levels
- Proposed channel drains

