




Skegness

CDC


P23-0012

Logistics Plan

1

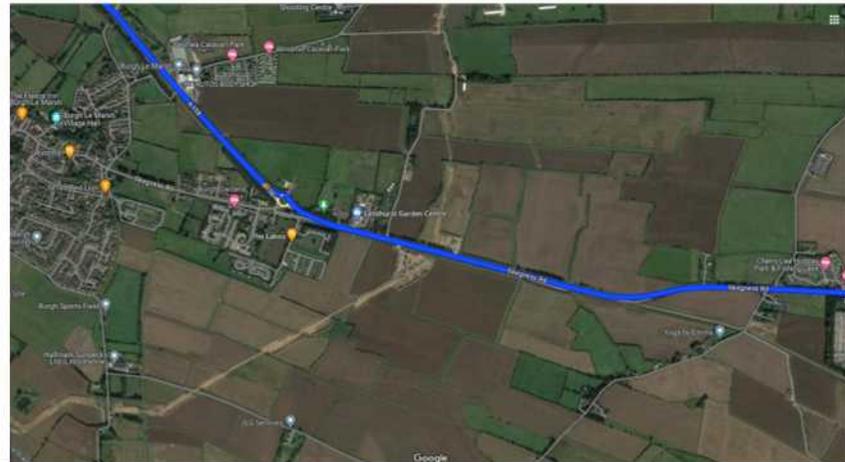

2

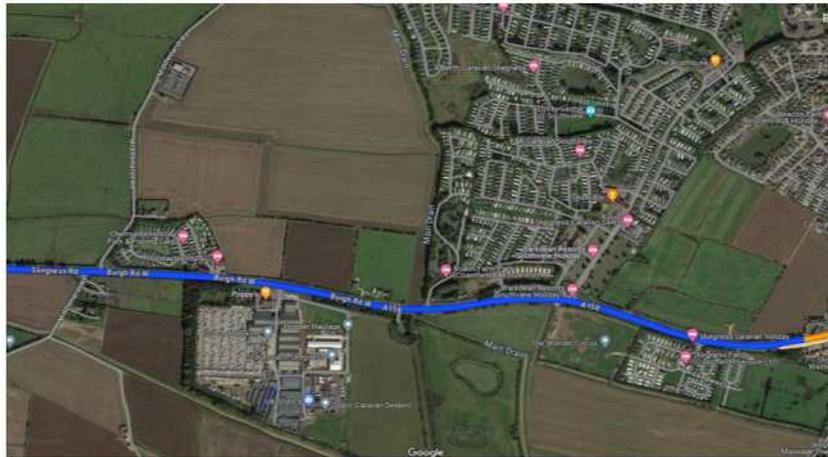

3



4



As shown on our mapping Plan, we have established the route into the site.

We can confirm with the route is adequate and does not involve any other width restrictions, low bridges or other traffic systems that hinder the delivery of our materials / Plant .

1



2




3



4



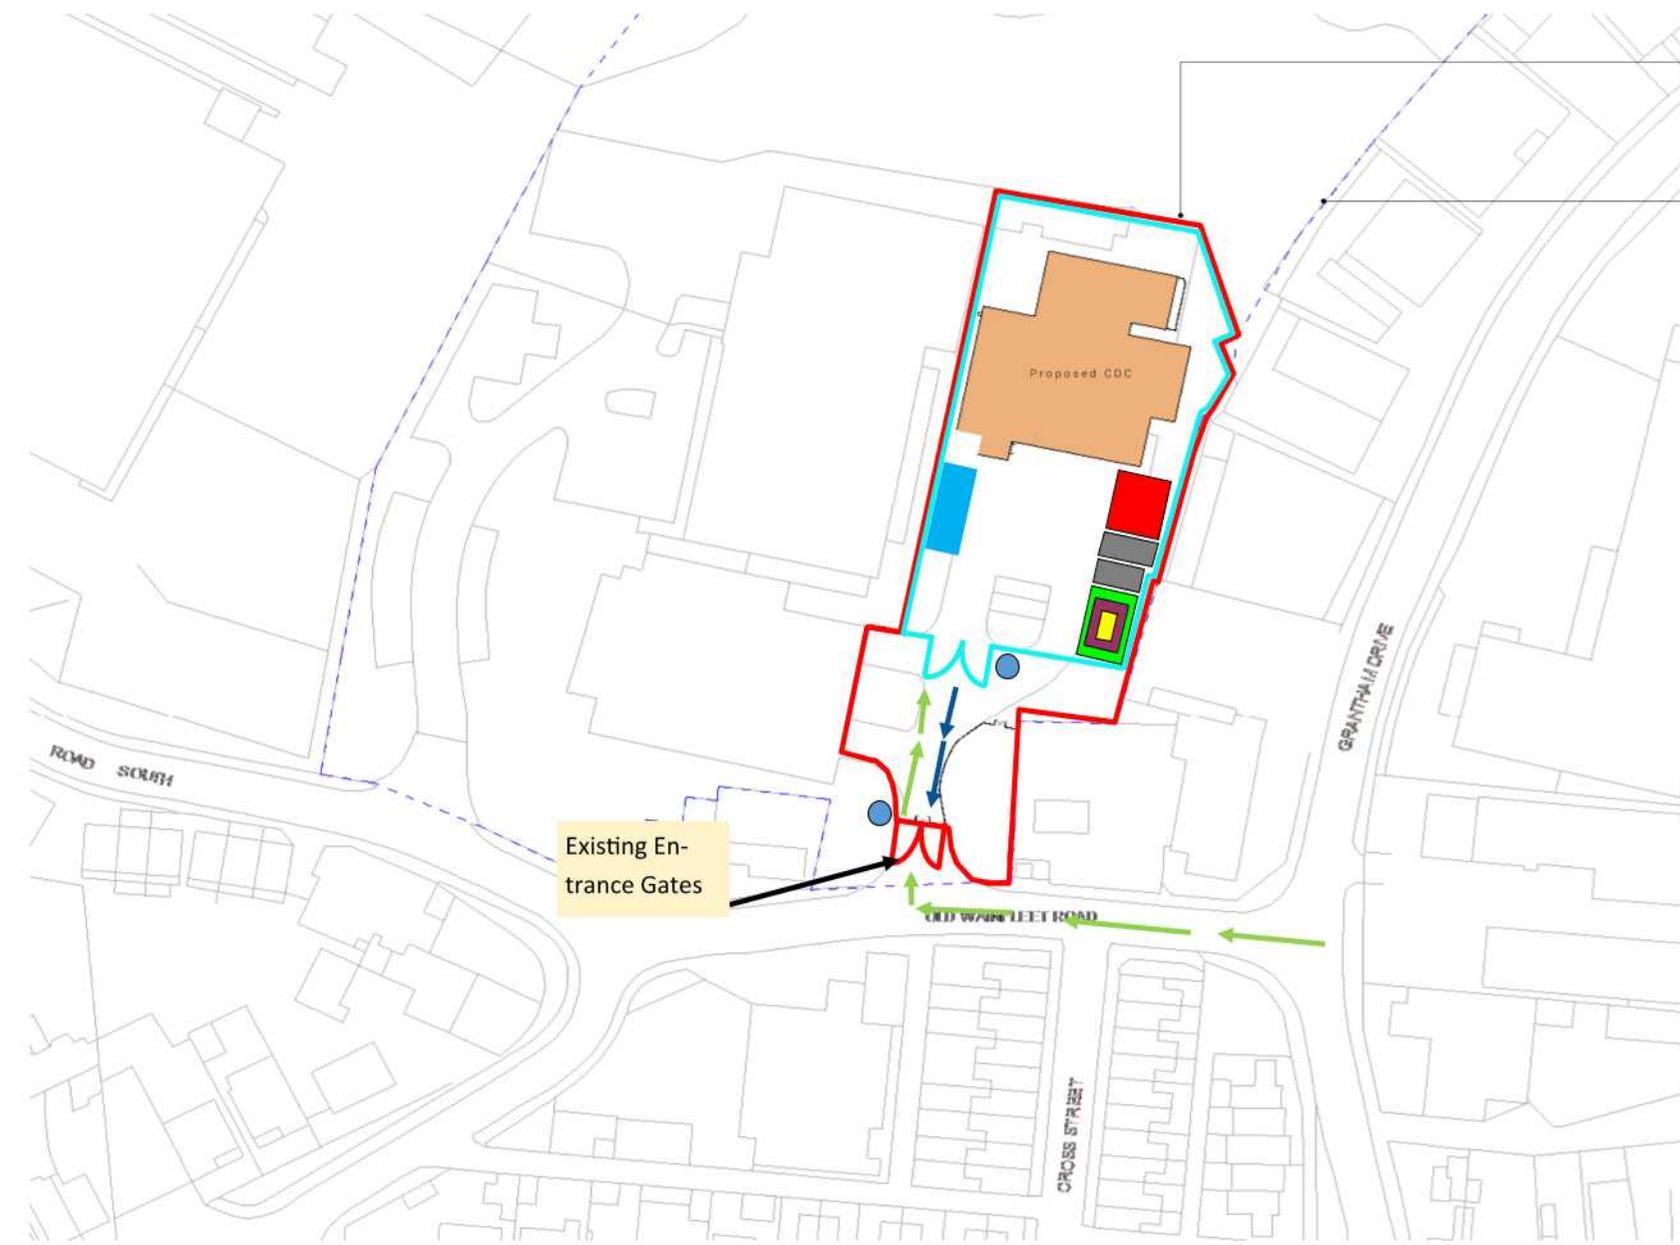


**Key**

- Route Into Site
- Route Out Of Site
- Logistics Area
- Site Boundary
- Site Area/ Compound Hoarding
- Site Waste
- Material Storage
- Site Offices
- Site Welfare
- Site Dry Room
- Banksman
- Contractor Parking
- Gate

MTX would use the proposed deliveries route to site for both material deliveries and modular drop offs, we would look to close the route during the modular lifts, we would propose weekend lifts to avoid causing congestion during peak times. MTX will make arrangements a week or two prior to any lift to have ensured all staff and patients are aware of the lift dates and times. We have proposed an area in which we have established as the vehicle manoeuvring zone which would be traffic managed by a qualified banksman, as well as making the area safe for pedestrians.

Level 00 - Location Plan

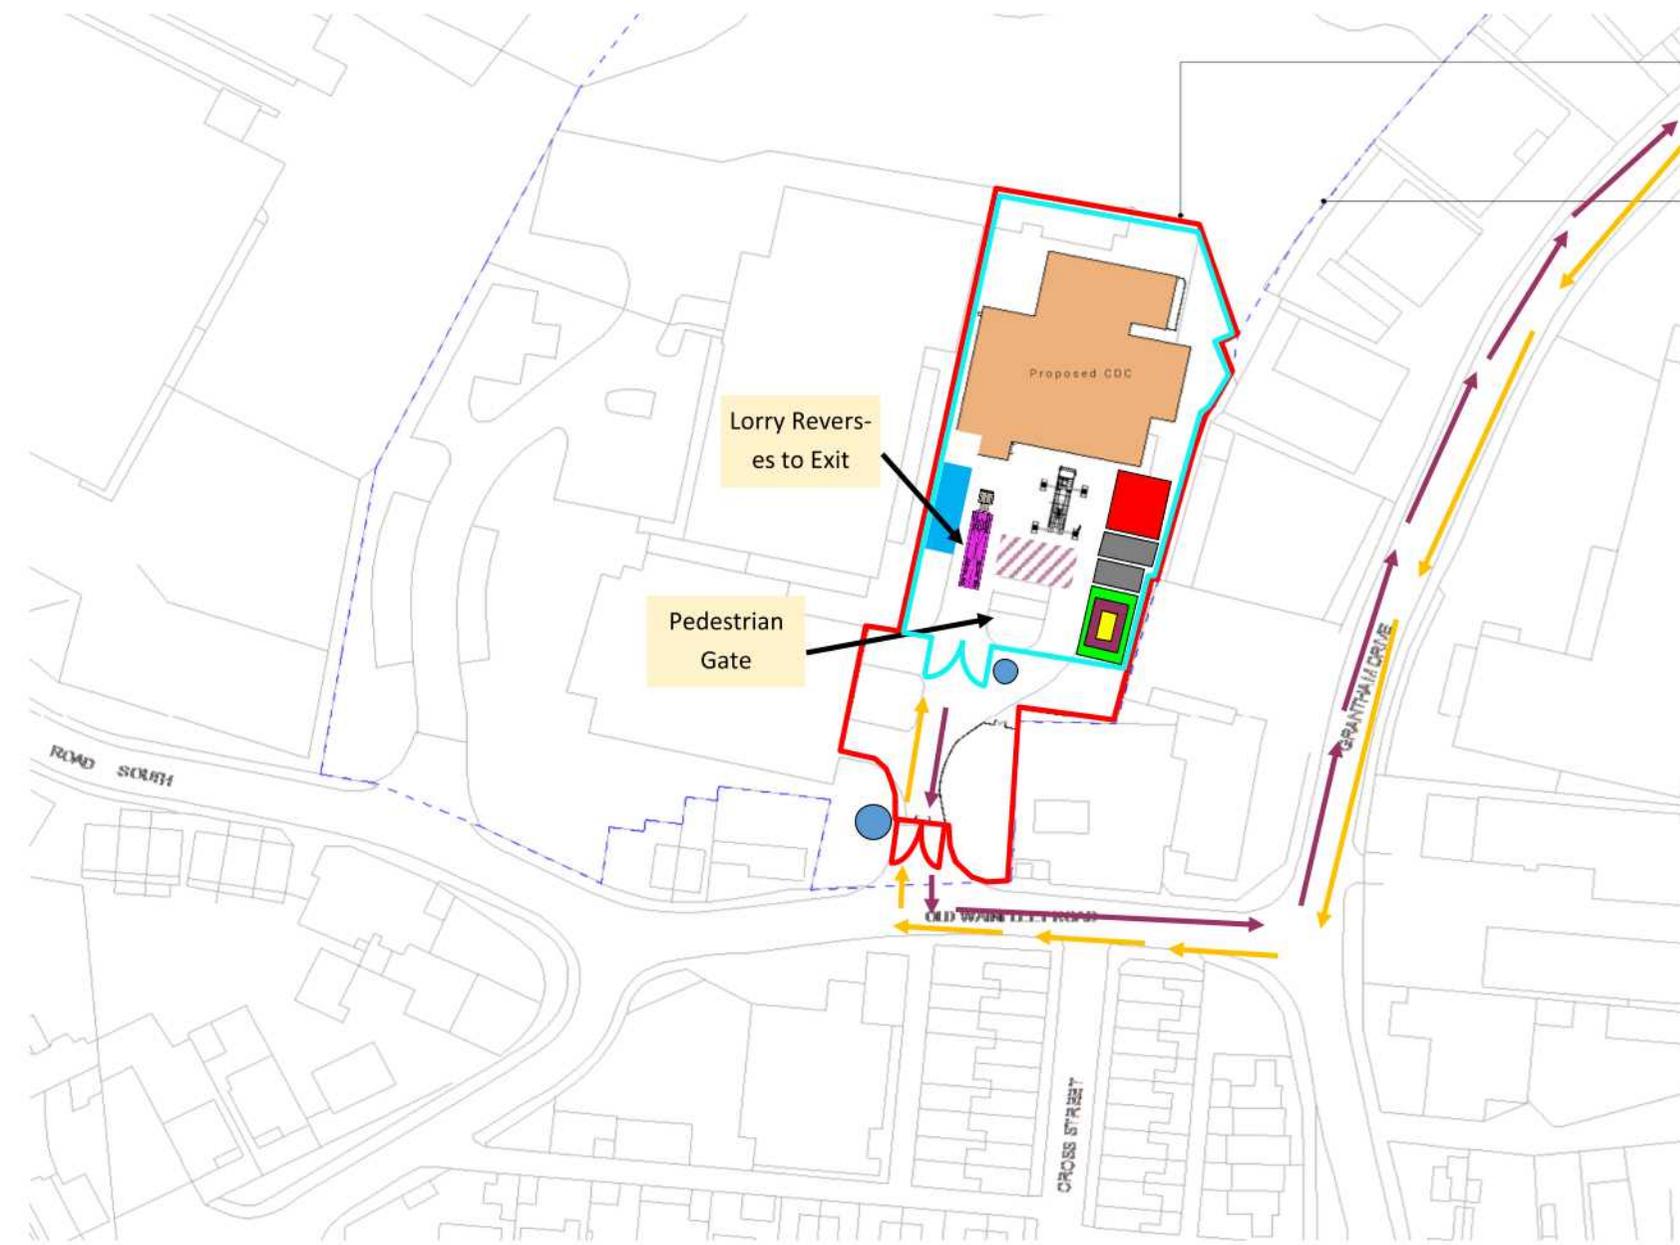


## Key

- Route Into Site
- Route Out Of Site
- Logistics Area
- Site Boundary
- Site Area/ Compound Hoarding
- Site Waste
- Material Storage
- Site Offices
- Site Welfare
- Site Dry Room
- Banksman
- Site Heras
- Contractor Parking
- Gate
- Crane Location
- Modular Drop-Off Point
- Modular Drop-Off Route (In)
- Modular Drop-Off Route (Out)


MTX would use the proposed deliveries route to site for both material deliveries and modular drop offs, we would look to close the route during the modular lifts, we would propose weekend lifts to avoid causing congestion during peak times. MTX will make arrangements a week or two prior to any lift to have ensured all staff and patients are aware of the lift dates and times. We have proposed an area in which we have established as the vehicle manoeuvring zone which would be traffic managed by a qualified banksman, as well as making the area safe for pedestrians.

Level 00 - Location Plan

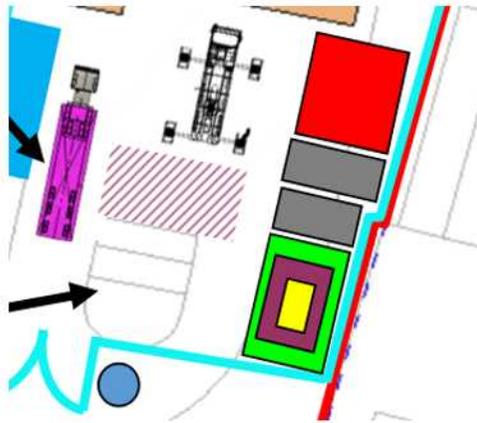

**Material Storage**

MTX use wide Industrial containers to safely and securely store any materials and equipment needed on site. The storage containers are monitored for the quants of items in storage and is locked before site is




**Site Welfare, Office & Dry Room**



MTX provide on site welfare facilities giving site staff a place take breaks, eat/Make food and male & Female WC as per the layout below. MTX have ensured these facilities are in line with Schedule 2 of the CDM regulations. A site dry room is provided as a secure place for staff to change if necessary and store personal belonging such a bags & clothing. Benches and coat hooks will also be providing within the dry room. MTX provide on site offices to allow on site meeting to take place, a safe place to store drawings and any legal documentation needed. We also provide an office for any subcontracts who may require a space to study drawings and discuss any method while on site.

