GA Page-Turner
Woodhayes Farm
Luppitt
Honiton
EX14 4TP.

Ref KT/24073updated

Date 16-Apr-21

Estimate

Dear Sir

Thank you for your enquiry, we enclose the following estimate for your consideration.

To supply and deliver to site: General purpose apex building with an overhang

Length 75'(22.86m) in 15'(4.572m) bays. **Width** 19'8"(6m)+4'(1.22m overhang) **Height to eaves** 9'10"(3m)
Pitch 15 Degrees

Side and end cladding. Clad with space boarding to ground level on one side and both ends.

Specifications

Columns:	203 x 102 x 23 Kg	Universal Beam
Rafters:	178 x 102 x 19 Kg	Universal Beam
Roof Bracing:	Both end bays.	C.H.S
Eaves Bracing:	50mm x 50mm	Angle
Eaves Purlins:	175mm x 75mm(C24)	Tanalised Timber
Main Purlins:	175mm x 75mm(C24)	Tanalised Timber
Roofing:	Eternit 2000 Fibre Cement 152mm corrugated	
Rooflights	10 no.	2.44Kg GRP
Guttering:	170mm Deep style P.V.C.	

Painted Steelwork Kit Form Price   **£10470.00** + V.A.T (Assuming a level site)
All steelwork finished with one undercoat and one gloss topcoat in green.

Hot Dip Galvanized Steelwork Kit Form Price   **£10760.00** + V.A.T. (Assuming a level site)

The additional price to supply Eternit Farmscape Anthracite coloured sheets would be: **£ 380.00** + V.A.T..

Yours faithfully

N Marshall
Terms and conditions of sale attached

N.B. If an architect's site visit were required to take levels/other details an extra cost would be incurred. Prices held for 28 days. List of experienced erectors available on request. The specification of this quote conforms to EN1090-1 and meets the legal requirements for European Conformity (CE) for agricultural buildings. E&OE, the seller reserves the right to amend the final price of the building subject to world fluctuations in steel prices between the signed confirmation of the order and delivery. If you have any queries regarding this estimate please do not hesitate to contact the undersigned.
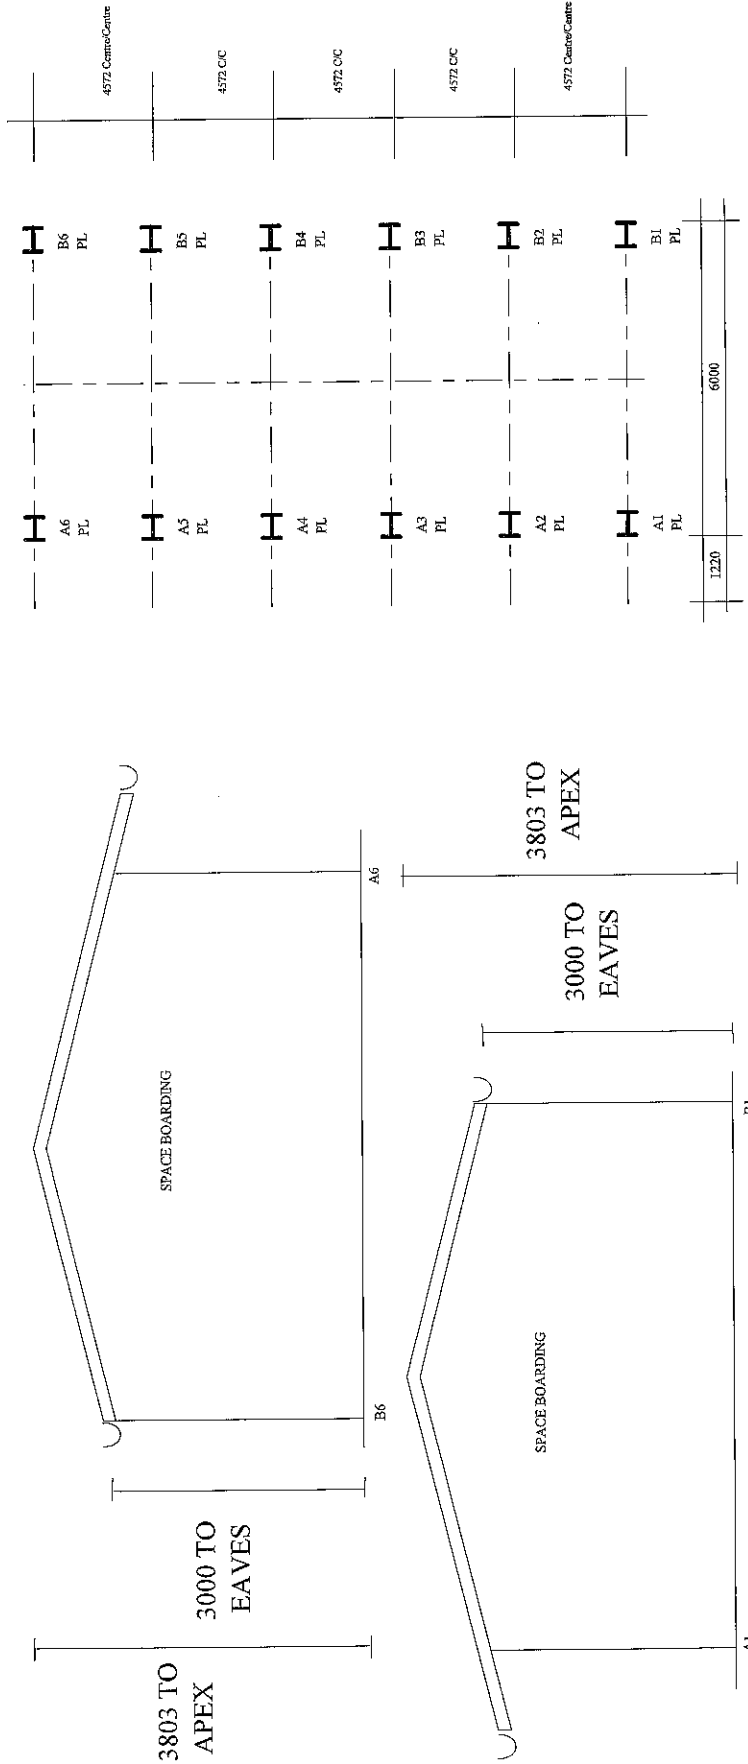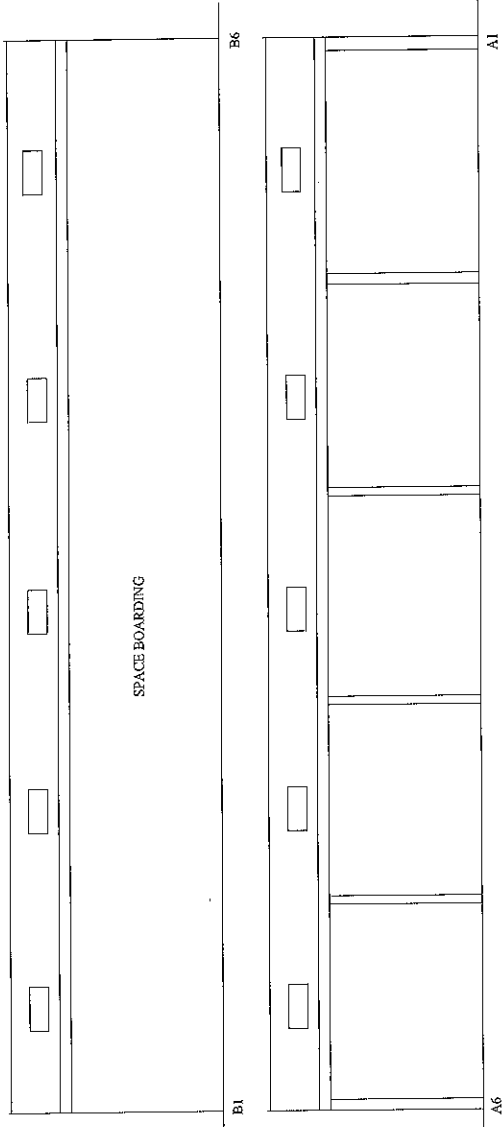
ETERNIT 2000 PROFILE 6 FIBRE CEMENT
WITH GRP ROOFLIGHTS

SPACE BOARDING

SPACE BOARDING

SPACE BOARDING

SPACE BOARDING

3803 TO APEX

3000 TO EAVES

3803 TO APEX

3000 TO EAVES

4572 Centre/Centre

4572 C/C

4572 C/C

4572 C/C

4572 Centre/Centre

6000

1220

B6 PL
B5 PL
B4 PL
B3 PL
B2 PL
B1 PL

A6 PL
A5 PL
A4 PL
A3 PL
A2 PL
A1 PL

B6
B1
A1
A6
