Corby - Shannon.mpp

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names
1		**Forrest Decommisioning - Mechanical Program**	**207.55 days?**	**Tue 06/04/21**	**Thu 30/09/21**	
2		**P 1 Wheat & Factory Services**	**207.55 days?**	**Tue 06/04/21**	**Thu 30/09/21**	
3		**Zone 1**	**50.55 days?**	**Tue 06/04/21**	**Wed 19/05/21**	
13		**Demo 213, 216, 218, 217**	**35.18 days**	**Mon 19/04/21**	**Wed 19/05/21**	
14		Enabling / Lifts - 218	5 days	Mon 19/04/21	Fri 23/04/21	Shannon Group
15		Demolition - 217	4 days	Tue 27/04/21	Fri 30/04/21	Shannon Group
16		Demolition 213	5 days	Fri 14/05/21	Wed 19/05/21	Shannon Group
18		**Zone 2**	**69 days?**	**Tue 06/04/21**	**Fri 04/06/21**	
31		**Demo 212, 231, 235, 241**				
32		Enabling Works 212, 241	13.18 days	Mon 12/04/21	Fri 23/04/21	Shannon Group
33		Demolition 235	12.36 days	Mon 17/05/21	Fri 28/05/21	Shannon Group
34		Demolition 231	25 days	Fri 14/05/21	Fri 04/06/21	Shannon Group
36		**Zone 3**	**35.55 days**	**Mon 19/04/21**	**Wed 19/05/21**	
47		**Demo 221, 222, 223, 224, 226**	**26.36 days**	**Tue 27/04/21**	**Wed 19/05/21**	
48		Demolition - Tank Farm, 226	5 days	Tue 27/04/21	Sat 01/05/21	Shannon Group
49		Demolition BH 3 - 221, 222, 22	10 days	Thu 29/04/21	Fri 07/05/21	Shannon Group
50		Demolition BH 1&2 - 223	5 days	Sun 16/05/21	Wed 19/05/21	Shannon Group
52		**Zone 4**	**103.18 days**	**Mon 12/04/21**	**Fri 09/07/21**	
64		**Demo - 227, 228, 229**	**85.82 days**	**Tue 27/04/21**	**Fri 09/07/21**	
65		Demolition PP Silos 229	5 days	Tue 27/04/21	Sat 01/05/21	Shannon Group
66		Demolition G3 Building - 227, 2	37.73 days	Mon 07/06/21	Fri 09/07/21	Shannon Group
68		**Zone 5**	**200.36 days**	**Mon 12/04/21**	**Thu 30/09/21**	
82		**Demo 232, 233, 234, 236**	**141.09 days**	**Wed 02/06/21**	**Thu 30/09/21**	
88		**Zone 6**	**175.82 days**	**Tue 06/04/21**	**Fri 03/09/21**	
100		**Demo 237, 238, 239, 240**	**70.36 days**	**Mon 05/07/21**	**Fri 03/09/21**	
101		Demolition 239, 240	2.45 days	Mon 05/07/21	Wed 07/07/21	Shannon Group
102		Demolition Pellet Silo	21.36 days	Mon 02/08/21	Fri 20/08/21	Shannon Group
103		Demolition 237	54.09 days	Mon 19/07/21	Fri 03/09/21	Shannon Group
105		**P 2 Glucose, Stores & CHP**	**203.64 days?**	**Tue 06/04/21**	**Mon 27/09/21**	
106		**Zone 7**	**24.18 days**	**Mon 12/04/21**	**Sun 02/05/21**	
109		**Asset Recovery 214**	**21.18 days**	**Thu 15/04/21**	**Sun 02/05/21**	
112		**Demo 214**	**21.18 days**	**Thu 15/04/21**	**Sun 02/05/21**	
113		Enabling Demo - 214	12.36 days	Thu 15/04/21	Sun 25/04/21	Shannon Group
114		Demolition - 214	6.82 days	Tue 27/04/21	Sun 02/05/21	Shannon Group
116		**Zone 8**	**151.73 days?**	**Wed 19/05/21**	**Sun 26/09/21**	
130		**Demo 210, 211**	**31.82 days**	**Mon 30/08/21**	**Sun 26/09/21**	
131		Demolition - 211	23.64 days	Mon 30/08/21	Sun 19/09/21	Shannon Group
132		Demolition - 210	23.64 days	Mon 06/09/21	Sun 26/09/21	Shannon Group
133		Demolition - 211 Silos	23.64 days	Mon 06/09/21	Sun 26/09/21	Shannon Group
135		**Zone 9**	**104.18 days**	**Mon 07/06/21**	**Sat 04/09/21**	
139		**Demo 206**	**36.64 days**	**Wed 04/08/21**	**Sat 04/09/21**	
140		Demolition - 206 [CHP]	27.55 days	Wed 04/08/21	Sat 04/09/21	Shannon Group
142		**Zone 10**	**91 days**	**Mon 21/06/21**	**Mon 06/09/21**	
151		**Demo GB 2**	**27.73 days**	**Sun 15/08/21**	**Mon 06/09/21**	
152		Demolition Gluscose 2	21.45 days	Sun 15/08/21	Mon 06/09/21	Shannon Group

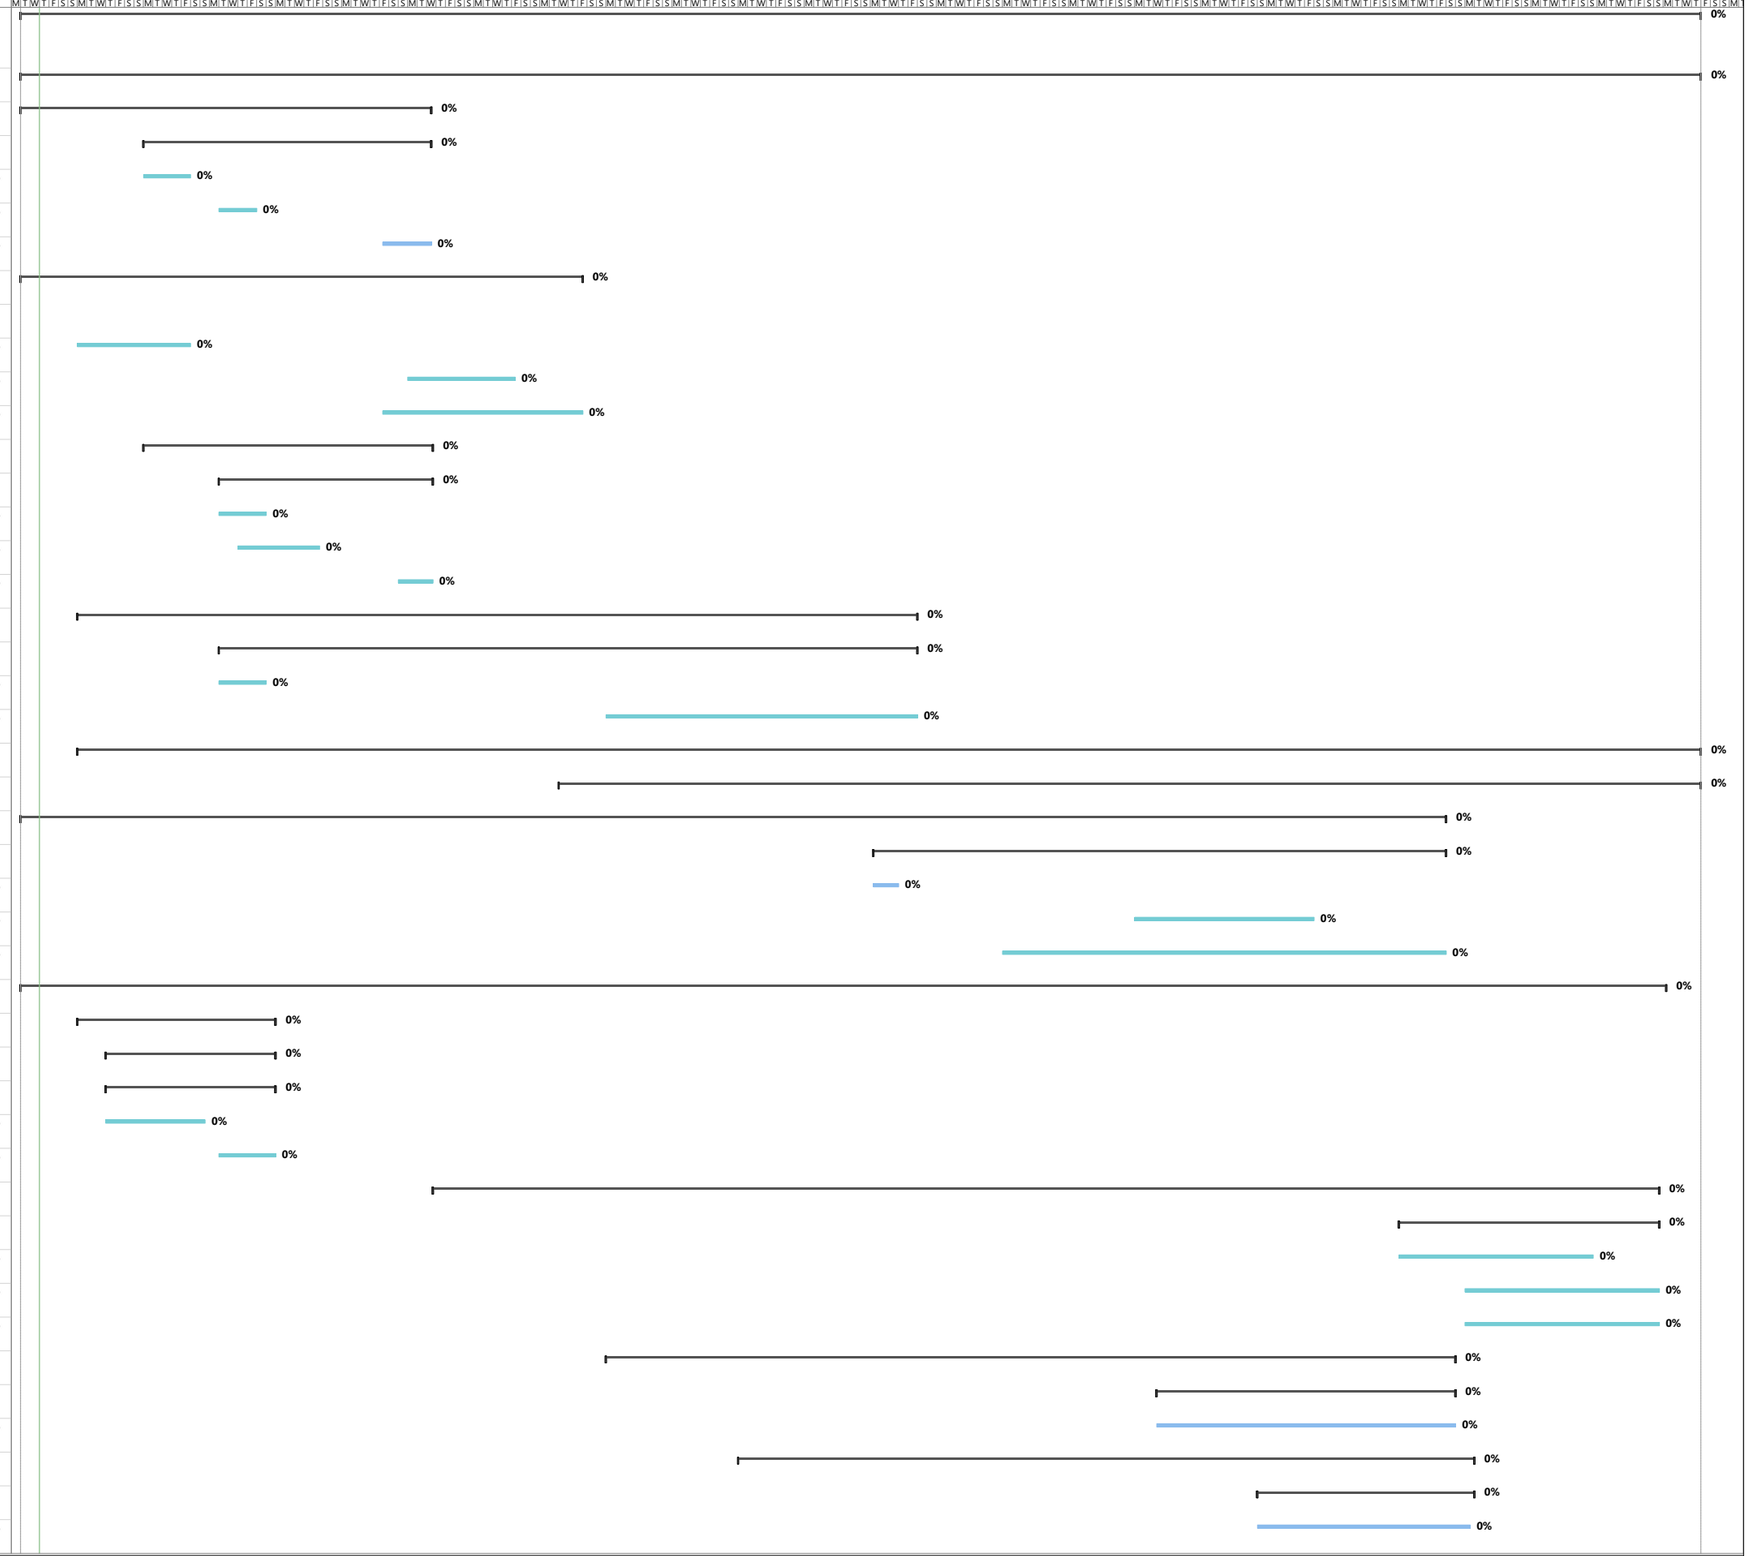

Critical | Critical Progress | Split | Manual Task | Finish-only | Baseline | Baseline Milestone | Summary Progress | Manual Summary | External Tasks | Inactive Task | Inactive Summary
Critical Split | Task | Task Progress | Start-only | Duration-only | Baseline Split | Milestone | Summary | Project Summary | External Milestone | Inactive Milestone | Deadline
